

Herricks Public Schools

July 2021 Bond Update Report



PARK EAST CONSTRUCTION

Prepared by John M. Mooney



Table of Contents

- ▶ **Section I** - Work Progress through July 2021
- ▶ **Section II** - Planned work for August 2021
- ▶ **Section III** - Progress Photos
- ▶ **Section IV** - Manpower Reports



Work Progress for July 2021

Fitness Center Addition HS

- ▶ All Exterior and Interior Masonry Work Complete
- ▶ All Cast Stone Installation Complete
- ▶ Roof Drains Installed
- ▶ Roof Drain Piping Installed w/Insulation
- ▶ Cold Water Lines Installed
- ▶ Retaining Wall Erected
- ▶ ATAS Framing and Insulation Complete
- ▶ Roofing Commenced



Work Progress for July 2021

Sitework Reconstruction Contract HS/MS

- ▶ HS Plaza & Island Demolition Complete
- ▶ New Gray Brick Veneer in HS Front Plaza Complete
- ▶ Asphalt Paving in HS Parking Lot Complete
- ▶ HS Front Plaza Concrete Flatwork and Curbing Complete
- ▶ MS Tennis Court Demolition Complete
- ▶ MS Bus Loop Demolition Complete
- ▶ MS Bus Curbs Complete



Work Progress for July 2021

Sitework Reconstruction Contract HS/MS

- ▶ MS Tennis Court Paving Complete
- ▶ MS Island Sidewalks & Curbing Complete
- ▶ MS Light Pole Conduit Installed
- ▶ 2 New ADA Ramps at MS Complete
- ▶ All MS Drainage Basins and Piping Complete
- ▶ All HS Drainage Basins and Piping Complete



Work Projected for August 2021

Fitness Center Addition at Herricks HS

- ▶ Complete Roofing
- ▶ Complete Priming and Blueskin Installation
- ▶ Install Perimeter Insulation and Backfill
- ▶ Install French Drains in Retaining Wall and Backfill
- ▶ Complete Excavation and Grading of Site
- ▶ Complete Concrete Work
- ▶ Demo Boys Locker Room Wall and Rebuild
- ▶ Complete Interior Framing
- ▶ Complete Spray Fireproofing
- ▶ Continue MEP Work on Interior



Work Projected for August 2021

Sitework Reconstruction Contract MS/HS

- ▶ Complete MS Grading and Paving
- ▶ Complete Sign Installation in Bus Loop
- ▶ Complete Tennis Court Paving
- ▶ Complete Tennis Court Fencing
- ▶ Complete Tennis Court Netting and Finished Surface
- ▶ Conclude Phase 4 MS Project



Work Projected for August 2021

Sitework Reconstruction Contract MS/HS

- ▶ Complete HS Curbing and Flatwork
- ▶ Install and Relocate HS Light Poles w/ New Conduit
- ▶ Complete HS Bus Loop Milling
- ▶ Complete RCA and Compaction of Bus Loop
- ▶ Complete Paving of HS Bus Loop
- ▶ Complete Striping of Bus Loop
- ▶ Complete Install of New Signage
- ▶ Conclude Phase 4 HS Project



Herricks Public Schools Construction Update Section III



July 2021 Construction Report



Fitness Center Masonry Complete



**Herricks Public Schools
Construction Update
Section III**




Roof Drains and Insulated Drain Piping Complete

July 2021 Construction Report



Herricks Public Schools Construction Update Section III

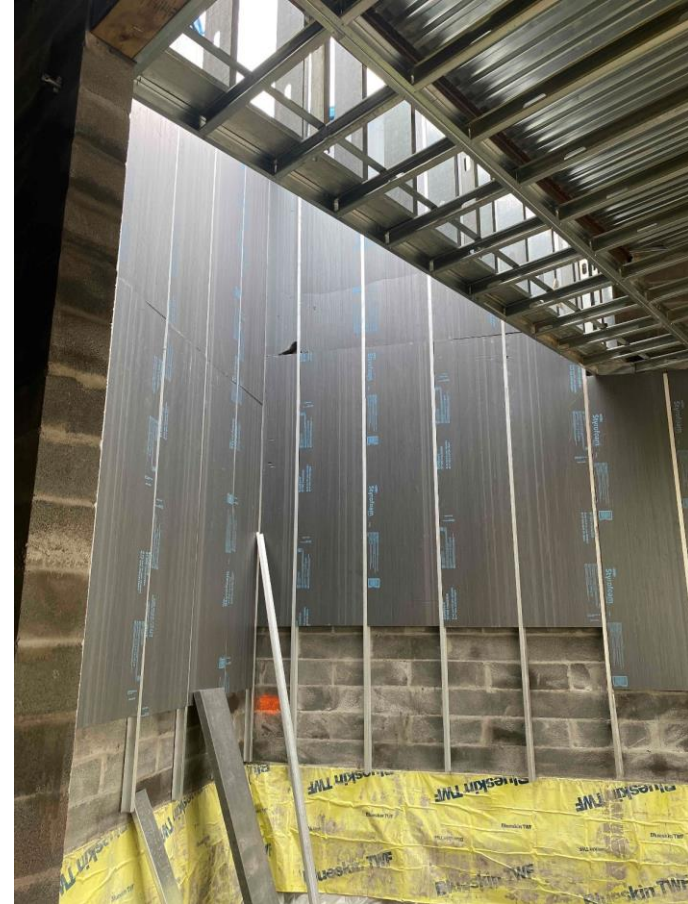

July 2021 Construction Report **ATAS Framing and Insulation Complete**¹¹



Retaining Wall Complete



Herricks Public Schools Construction Update Section III



HS Plaza Masonry Complete



HS Teachers Parking Lot Complete



HS Plaza Concrete & Curbing



MS Bus Curbs Complete



MS Island Sidewalks & Curbing Complete



Herricks Public Schools Construction Update Section III



July 2021 Construction Report **MS Tennis Court Paving Complete**
