

Herricks Union Free School District

2016 Capital Improvements Bond Update


May 25, 2017



Timeline to Date

December 6, 2016	Successful Bond Referendum Vote
December, 2016	BBS conducts field survey of existing interior doors and hardware with
January, 2017	District Facilities Director, and prepares construction documents for Phase I Capital Improvements. Synthetic turf field drawings are prepared and added to Phase I Capital Improvements package
February 21, 2017	Executed paperwork mailed to SED; Phase I logged in February 23, 2017
March 23, 2017	BBS Update to Board of Education
<u>May 25, 2017 Update:</u>	BBS requested a “Level 1” review for Phase I to expedite review process on April 4, 2017. SED expedites and conducts review on May 8, 2017. BBS preparing Addendum to SED for Phase I projects; projecting permit approval early June, 2017. Scheduled for late Summer, 2017 bidding.
	Survey & GPR work underway during April-early May of 2017. Survey data received BBS on May 10, 2017. Data incorporated into design documents for both Phase I and Phase II projects. Turf-field documents from Phase I submission now incorporate site survey & soils data for bidding purposes.

Updated Field Layout

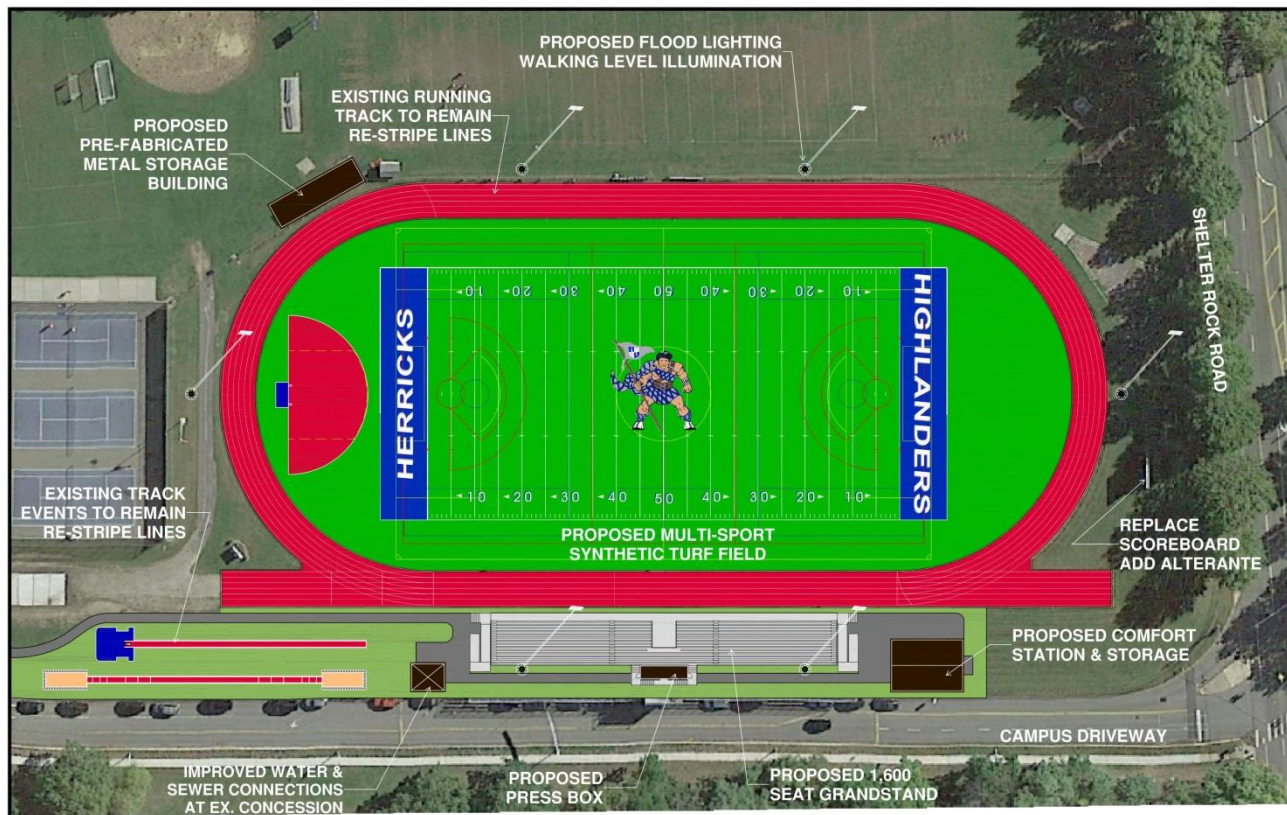

HERRICKS UNION FREE SCHOOL DISTRICT

PROPOSED HIGH SCHOOL SYNTHETIC TURF FIELD & ATHLETIC FACILITY IMPROVEMENTS

SEPTEMBER 28, 2016

rev. 04-20-17

Phase II projects underway for June submission

- **High School Cafeteria & Kitchen Renovations**
- **New 1,600-seat Bleachers and New Press Box at High School**
- **New Comfort Station Building at High School**
- **New Sports Storage Building at High School**
- **New Running Track Lighting at High School**
- Existing Concession Stand Rehabilitation at High School
- Selective Electrical Upgrades (service replacement) at High School
- Localized Ventilation Improvements – all schools
- Localized site drainage, asphalt & sidewalk improvements - all schools

Cafeteria Update since March, 2017

- 3/7/17** Initial questionnaire distributed to District representatives.
- 3/7-3/13/17** District publishes an on-line questionnaire for input from High School staff and students regarding cafeteria renovations.
- 3/7/17** BBS Kitchen Consultant field-visits and discusses existing kitchen parameters with District Food Services Director.
- 3/9/17** Initial “Open Forum” with District staff, students and members of the facilities committee to discuss results of District questionnaire and general likes and dislikes of current Cafeteria environment.
- 3/17/17** Follow-up meeting with District staff & students to review new floor plan concept.
- 3/23/17** BBS Update presentation to BOE.
- 4/20/17** Kitchen walkthrough with kitchen consultant, BBS and District / BOE representatives. Issues discussed and clarified; final kitchen plan presented & used for walkthrough.
- 5/8/17** Kitchen equipment modifications distributed at OACM meeting. Construction documents commence.

Moving Forward - Phase II Submission

6/5/17

BBS will electronically file Phase II projects as listed above to SED on 6/5/17.

Projects to be logged into SED queue and will be in system. Based on data available from SED website on 5/23/17, *“average time for final architectural review will be about 32-34 weeks.”*

(Note: This timeline is always subject to change, based on actual review time .)

End of January, 2018

Anticipated SED Review

As soon as permit is acquired, District can coordinate pre-purchase of kitchen equipment and have it in storage, ready for June, 2018 delivery to project site.

Herricks Union Free School District

Thank you

