

Herricks Union Free School District

2016 Capital Improvements Bond Update

July 19, 2018



Timeline to Date

December 6, 2016	Successful Bond Referendum Vote
December, 2016	BBS conducts field survey of existing interior doors and hardware with
January, 2017	District Facilities Director, and prepares construction documents for Phase I Capital Improvements. Synthetic turf field drawings are prepared and added to Phase I Capital Improvements package
February 21, 2017	Executed paperwork mailed to SED; Phase I logged in February 23, 2017
March 23, 2017	BBS Update to Board of Education
May 25, 2017	BBS Update to Board of Education BBS received a "Level 1" review for Phase I on April 4, 2017. Reviewed on May 8, 2017 Pre-Bid Addendum to SED sent; SED required update on NYSOPHP for Shelter Rock Academy, which is on Historic Register. SHPO approval obtained on July 18, 2017; Information to SED on July 18, 2017; final SED approval granted for late Summer, 2017 bidding as planned. Phase I work included new turf field & interior doors and hardware. This work currently completing.
July 31, 2017	Target Date for release to bid on Phase I Capital Improvements.
June 9, 2017	Phase II SED paperwork submitted and project submission made June 12, 2017. Phase II SED submission receives building permit. Project prepared for release to public bid. Out to Bid: 3/14/18; Bids Due: 4/4/18.

Current Phase II A projects under construction :

- High School Cafeteria & Kitchen Renovations
- New 1,600-seat Bleachers and New Press Box at High School
- New Comfort Station Building at High School
- New Sports Storage Building at High School
- New Running Track Lighting at High School

Phase II B projects submission – recently approved by NYSED

- Selective Electrical Upgrades (service replacement) at High School
- Localized Ventilation Improvements – all schools
- Localized site drainage, asphalt & sidewalk improvements - all schools
- **By filing for an expedited review with NYSED Facilities Planning, the District received building permit approvals for Phase IIB projects on June 26, 2018.**

Cafeteria Update – filing, approval & bidding

- 3/7/17 Initial questionnaire distributed to District representatives.
- 3/7-3/13/17 District publishes an on-line questionnaire for input from High School staff and students regarding cafeteria renovations.
- 3/7/17 BBS Kitchen Consultant field-visits and discusses existing kitchen parameters with District Food Services Director.
- 3/9/17 Initial “Open Forum” with District staff, students and members of the facilities committee to discuss results of District questionnaire and general likes and dislikes of current Cafeteria environment.
- 3/17/17 Follow-up meeting with District staff & students to review new floor plan concept.
- 3/23/17 BBS Update presentation to BOE.
- 4/20/17 Kitchen walkthrough with kitchen consultant, BBS and District / BOE representatives. Issues discussed and clarified; final kitchen plan presented & used for walkthrough.
- 5/8/17 Kitchen equipment modifications distributed at OACM meeting. Construction documents commence.
- 6/9/17 Phase II A submission, including cafeteria & kitchen renovations, made to SED. SED Review completed , and set to bid on 3/14/18.
- Phase II A bids were taken on 4/4/18.

Phase II A, II B and Phase III Projects

3/14/18 Phase II A Projects set to bid. Bids for Kitchen Equipment also taken.

4/4/18 Phase II A Projects Bids Taken.

4/17/18 Phase II A Bids Awarded via BOE Resolution.

Phase II B Projects (HS Electrical Upgrades, Localized Sitework Improvements and Localized HVAC Upgrades) received SED permits on June 26, 2018. Selective sitework at Denton is underway; balance of work to be discussed with District for an upcoming bidding period.

Phase III Projects

Phase III Projects are currently in completion of Contract Document Phase at BBS. These projects include:

Localized Window Replacements - Center Street ES, Denton Avenue ES, Searingtown ES, S/R Academy and Herricks HS

Localized Exterior Door Replacements – Center Street ES, Denton Ave ES, Searingtown ES, S/R Academy, Herricks HS, Herricks MS, Community Center

ADA Toilet Room Improvements – Center Street ES, Denton Ave ES and Searingtown ES

Selective Wall Improvements – Center Street ES, Denton Ave ES and Searingtown ES

Localized Plumbing Upgrades – Center Street ES, Searingtown ES, Herricks MS & Herricks HS

We anticipate SED submissions on these Phase III projects on or about 8/1/18.



Cafeteria Renovation - Update

The contract documents set was modified prior to SED submission to display the original artist's rendering lighting and ceiling layouts, as well as the other components of the room fit-out:

Folding wall entry area ("Nano-Wall"), allowing for opening up the adjoining corridor space leading to courtyard.

Multi-layered ceiling with concentric circles and pendant task lighting throughout; utilizing school colors (Royal Blue and White) within the ceiling planes

Bistro-style tables and seating, stack chairs and tables

Industrial inspired finishes incorporating neutral tones with pops of school colors.

Bid Awards include all of the above.

Cafeteria Renovation



Cafeteria Renovation



Cafeteria Renovation



Turf Field Completion – June, 2018



HERRICKS UNION FREE SCHOOL DISTRICT

PROPOSED HIGH SCHOOL SYNTHETIC TURF FIELD & ATHLETIC FACILITY IMPROVEMENTS

SEPTEMBER 28, 2016

rev. 04-20-17

Phase II A projects constitute this summer's work:

- **New 1,600-seat Grandstand and New Press Box at High School**
- **New Comfort Station Building at High School**
- **New Sports Storage Building at High School**
- **New Running Track Lighting at High School**
- **All of the above have been awarded to Landtek , the same site contractor who just completed the new turf field.**


Summer, 2018 – Construction Start on New Grandstand, Press Box & Walking Track Lighting



Summer, 2018 - Construction Underway on New Comfort Station



Summer, 2018 – Denton Avenue Elementary Parking Lot Reconstruction

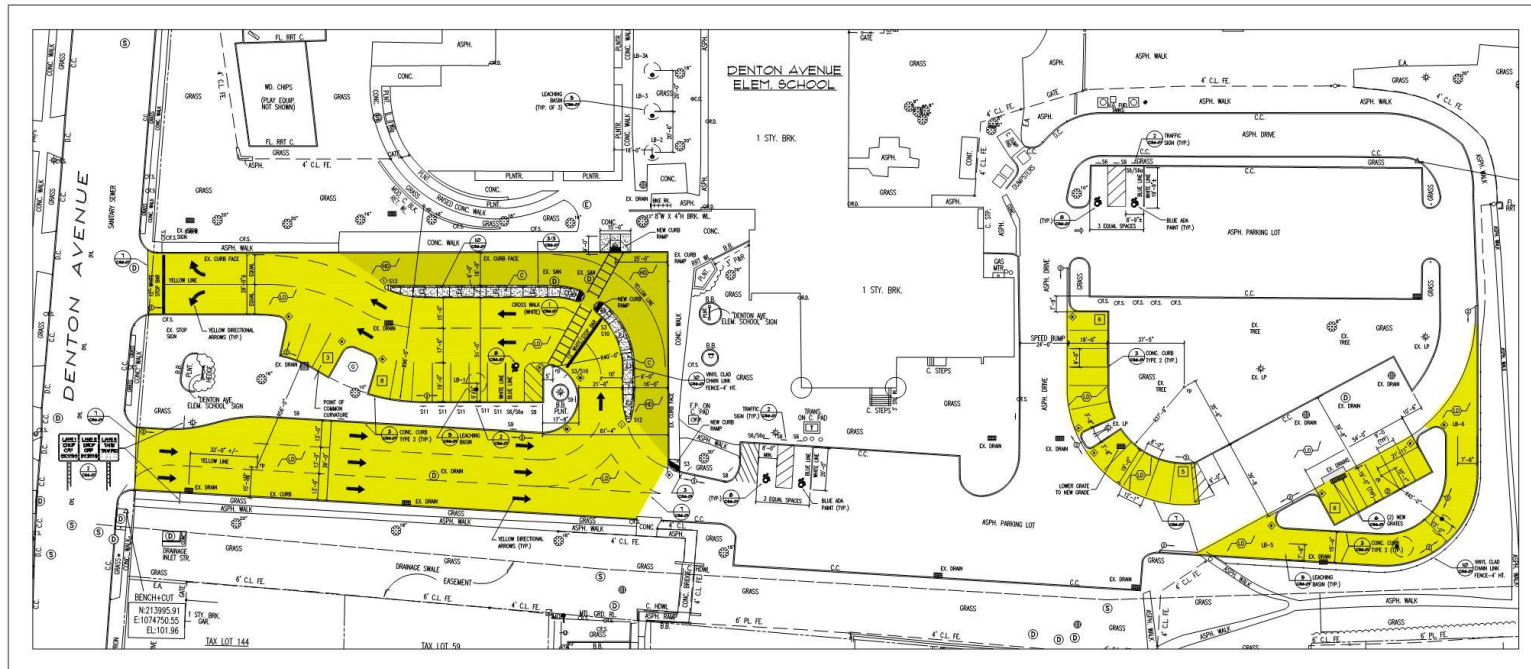

DENTON AVENUE PARKING AND BUS LOOP SITE PLAN

Herricks Union Free School District

Thank You

