### **Herricks Public Schools**

January 2021 Bond Update Report
Phase 3 High School Window Replacement and Fitness Center Addition





### **Table of Contents**

- Section I Work Progress through the January 2021
- Section II Planned work for February 2021
- Section III Progress Photos
- Section IV Manpower Reports



#### Work Progress for January 2021

#### Window replacement project at Herricks HS

General Contractor- Arrow steel Window corp.

- Completed installation of Architectural Window system on Elevation 19
- Completed installation of door numbers 5A and 8 on Architectural Drawings
- Began and completed 90% of all interior finish work on elevation 19 and 21, including break metal, ceiling trim, wall partition trim, and caulking
- Completed transmittal of attic stock now located in boiler room basement



#### Work Progress for January 2021

#### Fitness Center Addition at Herricks HS

- Complete site demolition of concrete flatwork and trees relevant to retaining wall construction
- Strip and remove/stockpile existing topsoil
- Excavation and installation for new storm water drainage structures, sand collars, and piping between the same
- Excavation commenced for new building foundation



#### Work Projected for February 2021

#### Window replacement project at Herricks HS

Window Replacement Contractor - Arrow Steel Window Corp.

- Complete 100% of all interior finish work on all elevations
- Complete Re-Installation of (4) AC Split units on elevation 19
- Complete Re-Connect of all electrical fixtures on elevation 19
- Complete all items on PEC observation list and BBS punch list
- Begin project closeout and final documentation



#### Work Projected for February 2021

#### Fitness Center Addition at Herricks HS

- Extension and relocation of existing sanitary drainage structures
- Commence concrete footings and foundation walls for new foundation
- Installation of new power supply conduit from existing electrical service to approximate area of addition and new step-down transformer
- Commence under-slab electrical and plumbing rough-ins







Interior Finish Work









Gymnasium Door Installation



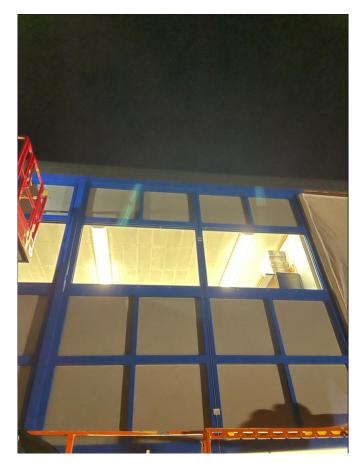

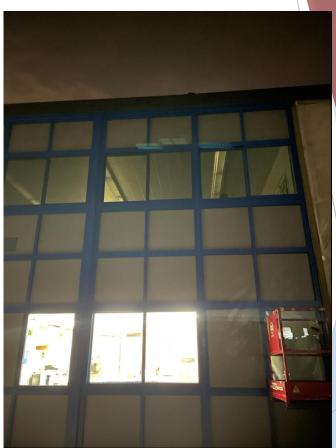

**Elevation 19 Window Installation** 







**Elevation 19 Window Interior** 







**Elevation 19 Window Interior** 







Demolition and removal of cellar entrance handrail and all concrete flatwork in project scope







Tree removal and install of erosion control screen on south hillside







Installation of new precast concrete stormwater drainage structures








Survey and excavation of new building footprint for concrete footings and foundations



### **HS Window Replacement Manpower log**

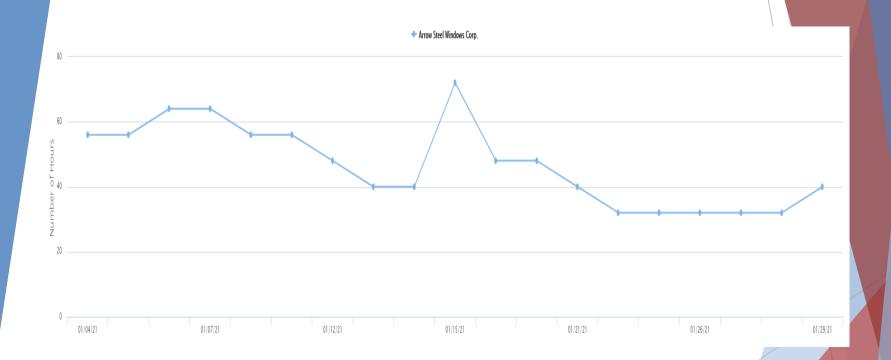

January 2021

16



### **HS Fitness Center Manpower log**

#### rio i itiless sentei manpowei iog

