

# **Herricks Public Schools**

May 20<sup>th</sup> 2021 BOE Update Report



**PARK EAST CONSTRUCTION**

**Prepared by Brandon Weisberg**



# Table of Contents

- ▶ **Section I** - Work Progress
- ▶ **Section II** – Planned Upcoming Work
- ▶ **Section III** – Progress Photos



## Notable Work Progress

### Fitness Center Addition at Herricks HS

- ▶ Completed Foundation Backfill and Compaction
- ▶ Formed & Poured Outlying Pier
- ▶ Installed Subgrade Roof Drain & Sanitary Line
- ▶ Completed In-Slab Electrical Conduit Fabrication & Layout
- ▶ Erected All Structural Steel
- ▶ Installed All Roof Decking
- ▶ Third Party Structural Inspections Completed and Approved
- ▶ Sub slab vapor barrier and associated inspections



## **Notable Work Planned/Upcoming**

### **Fitness Center Addition at Herricks HS**

- ▶ Commence exterior and interior masonry block walls
- ▶ Install Roofing System & Curbing for HVAC Units
- ▶ Upon roofing completion, spray applied fireproofing as necessary
- ▶ Mechanical, Electrical, and Plumbing rough-ins throughout block walls as necessary (simultaneous with installation)

### **Sitework Contract at HHS and HMS (Summer Start)**



## Herricks Public Schools Fitness Center Addition Section III




### Foundation Backfill & Compaction





## Herricks Public Schools Fitness Center Addition Section III

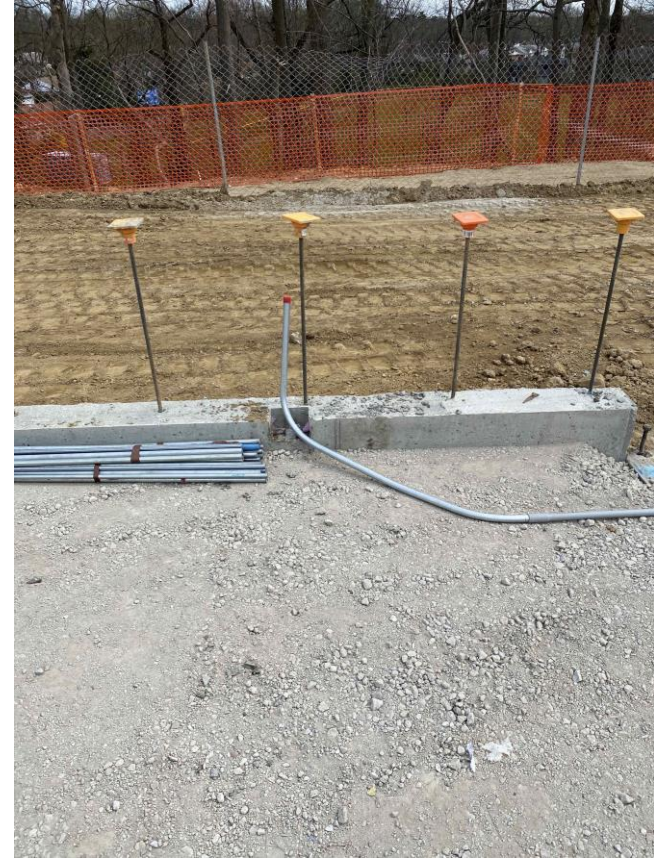

### Conduit Fabrication & Layout





## Herricks Public Schools Fitness Center Addition Section III



### Steel Columns and Beams Crane Operations

May 21 BOE Update



## Herricks Public Schools Fitness Center Addition Section III



### Progress of Steel Columns, Beams, and Joists





## Herricks Public Schools Fitness Center Addition Section III



Completed Steel Columns, Beams, and Metal Decking



**Under-slab vapor barrier and in-slab electrical conduit**





## Herricks Public Schools Fitness Center Addition Section III



Concrete Slab Poured





**Concrete Slab Poured**
