

Herricks Union Free School District

2016 Capital Improvements Bond Update

November 19, 2020

Timeline to Date

December 6, 2016	Successful Bond Referendum Vote
December, 2016	BBS conducts field survey of existing interior doors and hardware with District
January, 2017	Facilities Director and prepares construction documents for Phase I Capital Improvements. Synthetic turf field drawings are prepared and added to Phase I Capital Improvements package.
February 21, 2017	Executed paperwork mailed to SED; Phase I logged in February 23, 2017
March 23, 2017	BBS Update to Board of Education
May 25, 2017	BBS Update to Board of Education BBS received a "Level 1" review for Phase I on April 4, 2017. Reviewed on May 8, 2017 Pre-Bid Addendum to SED sent; SED required update on NYSOPHP for Shelter Rock Academy (on Historic Register) SHPO approval obtained on July 18, 2017; information to SED on July 18, 2017; final SED approval granted for late Summer, 2017 bidding as planned. Phase I work included new turf field & interior doors and hardware. This work currently completing.
July 31, 2017	Target Date for release to bid on Phase I Capital Improvements.
June 9, 2017	Phase II SED paperwork submitted and project submission made June 12, 2017. Phase II SED submission receives building permit. Project prepared for release to public bid. Out to Bid: 3/14/18; Bids Due: 4/4/18.



Timeline to Date

February 13, 2018

Phase IIB – Localized Ventilation Improvements at Center St ES, Denton Ave ES, Searingtown ES, Herricks High School & Rock Academy submitted to SED. Project Approved by SED on June 26, 2018. Work began Summer, 2019 and completed in Spring, 2020.

February 13, 2018

Phase IIB – Localized Parking Lot & Sitework at Center St ES, Searingtown ES, & Shelter Rock Academy submitted to SED. Project Approved by SED on June 26, 2018; work took place Summer, 2019.

October 11, 2018

Phase III – Selective Interior Wall Improvements at Herricks High School, Center St ES, Denton Ave ES & Searingtown ES submitted to SED. Project Approved by SED on November 28, 2018; Bids taken 5/2/19; District handling via County Contract.

October 11, 2018

Phase III – Localized Window Replacements at Center St ES, Denton Ave ES & Searingtown ES submitted to SED. Project Approved by SED on November 28, 2018; Bids taken on 5/9/19. Work Completed in Spring, 2020.

November 13, 2018

Phase III – Localized Plumbing Upgrades at Center St ES, Searingtown ES, Herricks High School & Middle School submitted to SED. Project Approved by SED on March 11, 2019. District is handling projects in-house.



Timeline to Date

November 13, 2018

Phase III – Selective Toilet Renovations at Center St ES, Denton Ave ES & Searingtown ES submitted to SED. Project Approved by SED on March 11, 2019. Bids taken 4/11/19. District handled projects in-house.

November 21, 2018

Phase III - High School Localized Window Replacements submitted to SED. Project Approved by SED on March 6, 2019. Set to bid on 4/17/19. Bids rejected, and project was re-bid on 5/28/19. Awarded, and work is currently in construction.

June 26, 2019

Phase IV – New Fitness Center at Herricks High School submitted to SED. Project Approved by SED on December 18, 2019. Bids taken 3/5/20 & rejected. Project rebid on 7/16/20 & awarded. Construction just starting.

March 2, 2020

Phase IV - Localized Masonry Repairs at HHS & HMS and Site Improvements at High School & Middle School submitted to SED. Projects Approved by SED on April 7, 2020. Bids received on 7/16/20; both projects to be re-bid at a later date.



Phase I projects included:

- New High School Turf Field – completed June, 2018 – Grand Opening was for Homecoming, 2018



Phase IIA Projects included:

- New Grandstand, Press Box & Walking Track Lighting – completed October, 2018 Grand Opening was for Homecoming, 2018



Phase IIA Projects included:

- New Comfort Station – completed October, 2018 Grand Opening was for Homecoming, 2018



Phase II A projects completed :

- New 1,600-seat Bleachers and New Press Box at High School
- New Comfort Station Building at High School
- New Sports Storage Building at High School
- New Running Track Lighting at High School
- High School Cafeteria & Kitchen Renovations – opened September, 2018

3/14/18 Phase II A Projects set to bid. Bids for Kitchen Equipment also taken.

4/4/18 Phase II A Projects Bids Taken.

4/17/18 Phase II A Bids Awarded via BOE Resolution. Project Substantially Complete on 9/4/18.

Phase II B Projects (HS Electrical Upgrades, Localized Sitework Improvements and Localized HVAC Upgrades) received SED permits on June 26, 2018. Selective sitework at Denton completed; balance of sitework was also bid & awarded; with the balance of work bid done for Summer, 2019 construction.



Cafeteria Update – filing, approval & bidding – **Project Completed**

- 3/7/17 Initial questionnaire distributed to District representatives.
- 3/7-3/13/17 District publishes an on-line questionnaire for input from High School staff and students regarding Cafeteria renovations.
- 3/7/17 BBS Kitchen Consultant field-visits and discusses existing kitchen parameters with District Food Services Director.
- 3/9/17 Initial “Open Forum” with District staff, students and members of the facilities committee to discuss results of District questionnaire and general likes and dislikes of current Cafeteria environment.
- 3/17/17 Follow-up meeting with District staff & students to review new floor plan concept.
- 3/23/17 BBS Update presentation to BOE.
- 4/20/17 Kitchen walkthrough with kitchen consultant, BBS and District / BOE representatives. Issues discussed and clarified; final kitchen plan presented & used for walkthrough.
- 5/8/17 Kitchen equipment modifications distributed at OACM meeting. Construction documents commenced.
- 6/9/17 Phase II A submission, including cafeteria & kitchen renovations, made to SED. SED Review completed, project was set to bid on 3/14/18. Phase II A bids were taken on 4/4/18. Summer construction took place, and **Cafeteria re-opened in September, 2018. Project Completed.**

Slide 9


SW1

Steven Walsh, 11/15/2020

Cafeteria Renovation



**Summer, 2018 – Denton Avenue Elementary
Parking Lot Reconstruction – Completed for September, 2018**

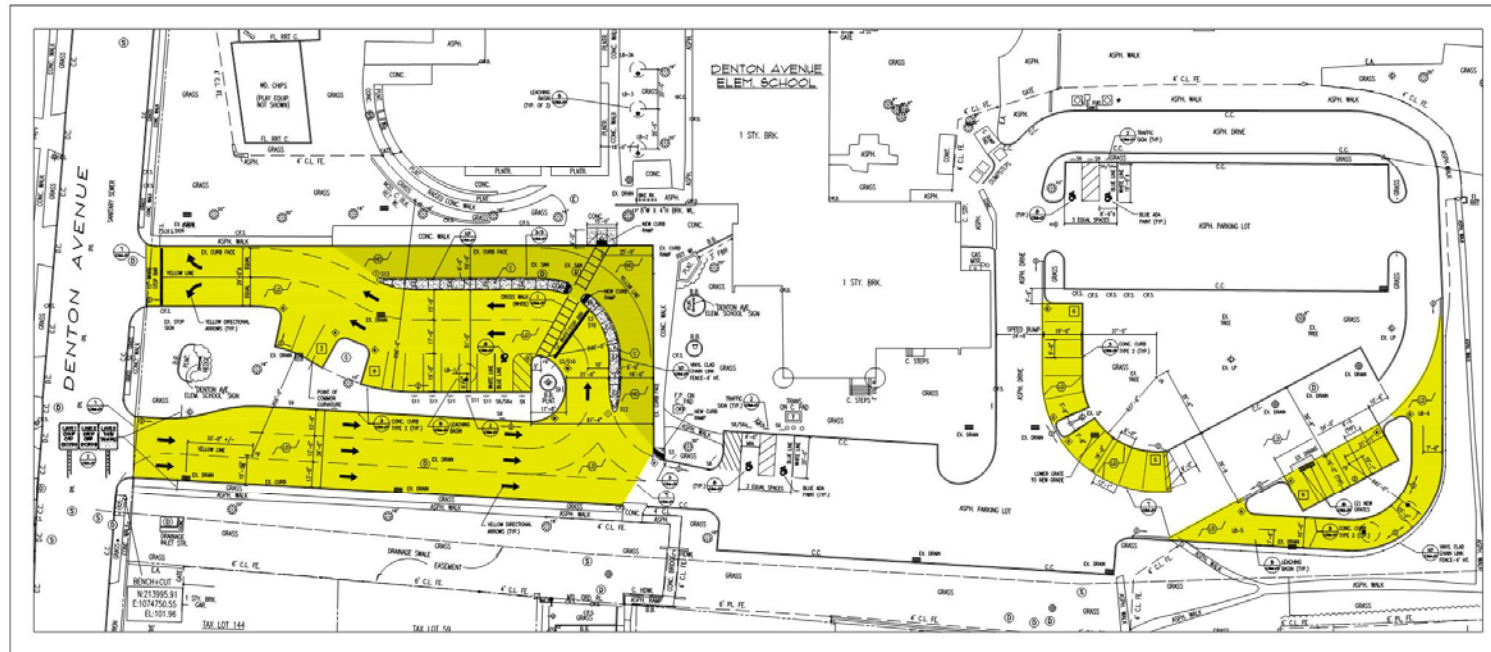

DENTON AVENUE PARKING AND BUS LOOP SITE PLAN

Phase II B projects completed – Summer, 2019

- Selective Electrical Upgrades (service replacement) at High School
- Localized Ventilation Improvements – at Center Street ES, Denton Avenue ES, Searingtown ES, Herricks High School and Shelter Rock Academy
- Localized site drainage, asphalt & sidewalk improvements - elementary schools & Shelter Rock Academy; Community Center was funded by a grant in April, 2018.



Phase II B projects completed – Summer, 2019

- Selective Electrical Upgrades (service replacement) at High School
- Localized Ventilation Improvements – at Center Street ES, Denton Avenue ES, Searingtown ES, Herricks High School and Shelter Rock Academy
- Localized site drainage, asphalt & sidewalk improvements - elementary schools & Shelter Rock Academy; Community Center was funded by a grant in April, 2018.



Phase II B projects completed – Summer, 2019

- Selective Electrical Upgrades (service replacement) at High School
- Localized Ventilation Improvements – at Center Street ES, Denton Avenue ES, Searingtown ES, Herricks High School and Shelter Rock Academy
- Localized site drainage, asphalt & sidewalk improvements - elementary schools & Shelter Rock Academy; Community Center was funded by a grant in April, 2018.



Phase III Projects - Active / Completing

Phase III Projects were either bid and awarded or done by District Facilities staff in-house since the last Bond Update held on 9/27/2018. These projects include:

Localized Window Replacements - Center Street ES, Denton Avenue ES & Searingtown ES (work completed Spring, 2020) and Herricks HS (currently in construction).

Localized Exterior Door Replacements – Center Street ES, Denton Ave ES, Searingtown ES, S/R Academy, Herricks HS, Herricks MS, Community Center – these projects are being handled either through Facilities with local vendor on contract – or – were included with localized window replacements projects.

ADA Toilet Room Improvements – Center Street ES, Denton Ave ES & Searingtown ES – done through District Facilities in-house staff, as bids received were cost-prohibitive.

Selective Wall Improvements – Center Street ES, Denton Ave ES & Searingtown ES - currently being priced out by County Contract pre-established vendor (P&M Door Corp.)

Localized Plumbing Upgrades – Center Street ES, Searingtown ES, Herricks MS & Herricks HS - done through District Facilities with pre-established vendor on as-needed basis.

High School Science Lab 708 – Renovation done through District Facilities in-house staff.



Phase III Projects - Active / Completing

Phase III Projects were either bid and awarded or done by District Facilities staff in-house since the last Bond Update held on 9/27/2018. These projects include:

Localized Window Replacements - Center Street ES, Denton Avenue ES & Searingtown ES (work completed Spring, 2020) and Herricks HS (currently in construction).



Phase III Projects - Active / Completing

Phase III Projects were either bid and awarded or done by District Facilities staff in-house since the last Bond Update held on 9/27/2018. These projects include:

Localized Window Replacements - Center Street ES, Denton Avenue ES & Searingtown ES (work completed Spring, 2020) and Herricks HS (currently in construction).



Phase III Projects - Active / Completing

Phase III Projects were either bid and awarded or done by District Facilities staff in-house since the last Bond Update held on 9/27/2018. These projects include:

Localized Window Replacements - Center Street ES, Denton Avenue ES & Searingtown ES (work completed Spring, 2020) and Herricks HS (currently in construction).



Phase III Projects - Active / Completing

Phase III Projects were either bid and awarded or done by District Facilities staff in-house since the last Bond Update held on 9/27/2018. These projects include:

Localized Window Replacements - Center Street ES, Denton Avenue ES & Searingtown ES (work completed Spring, 2020) and Herricks HS (currently in construction).



Phase IV Projects – to be re-bid

Herricks High School and Herricks Middle School Localized Masonry Repairs

On July 16, 2020, bids were taken for proposed Localized Masonry Repairs at Herricks High School & Herricks Middle School.

Due to inconsistencies in the submitted bids, this work will require future re-bidding.

Herricks High School and Herricks Middle School Parking & Bus Loop Improvements

On July 16, 2020, bids were taken for proposed Localized Masonry Repairs at Herricks High School & Herricks Middle School.


Due to inconsistencies in the submitted bids, this work will require future re-bidding.



Phase IV Projects – to be re-bid

Existing Site Aerial


Herricks High School

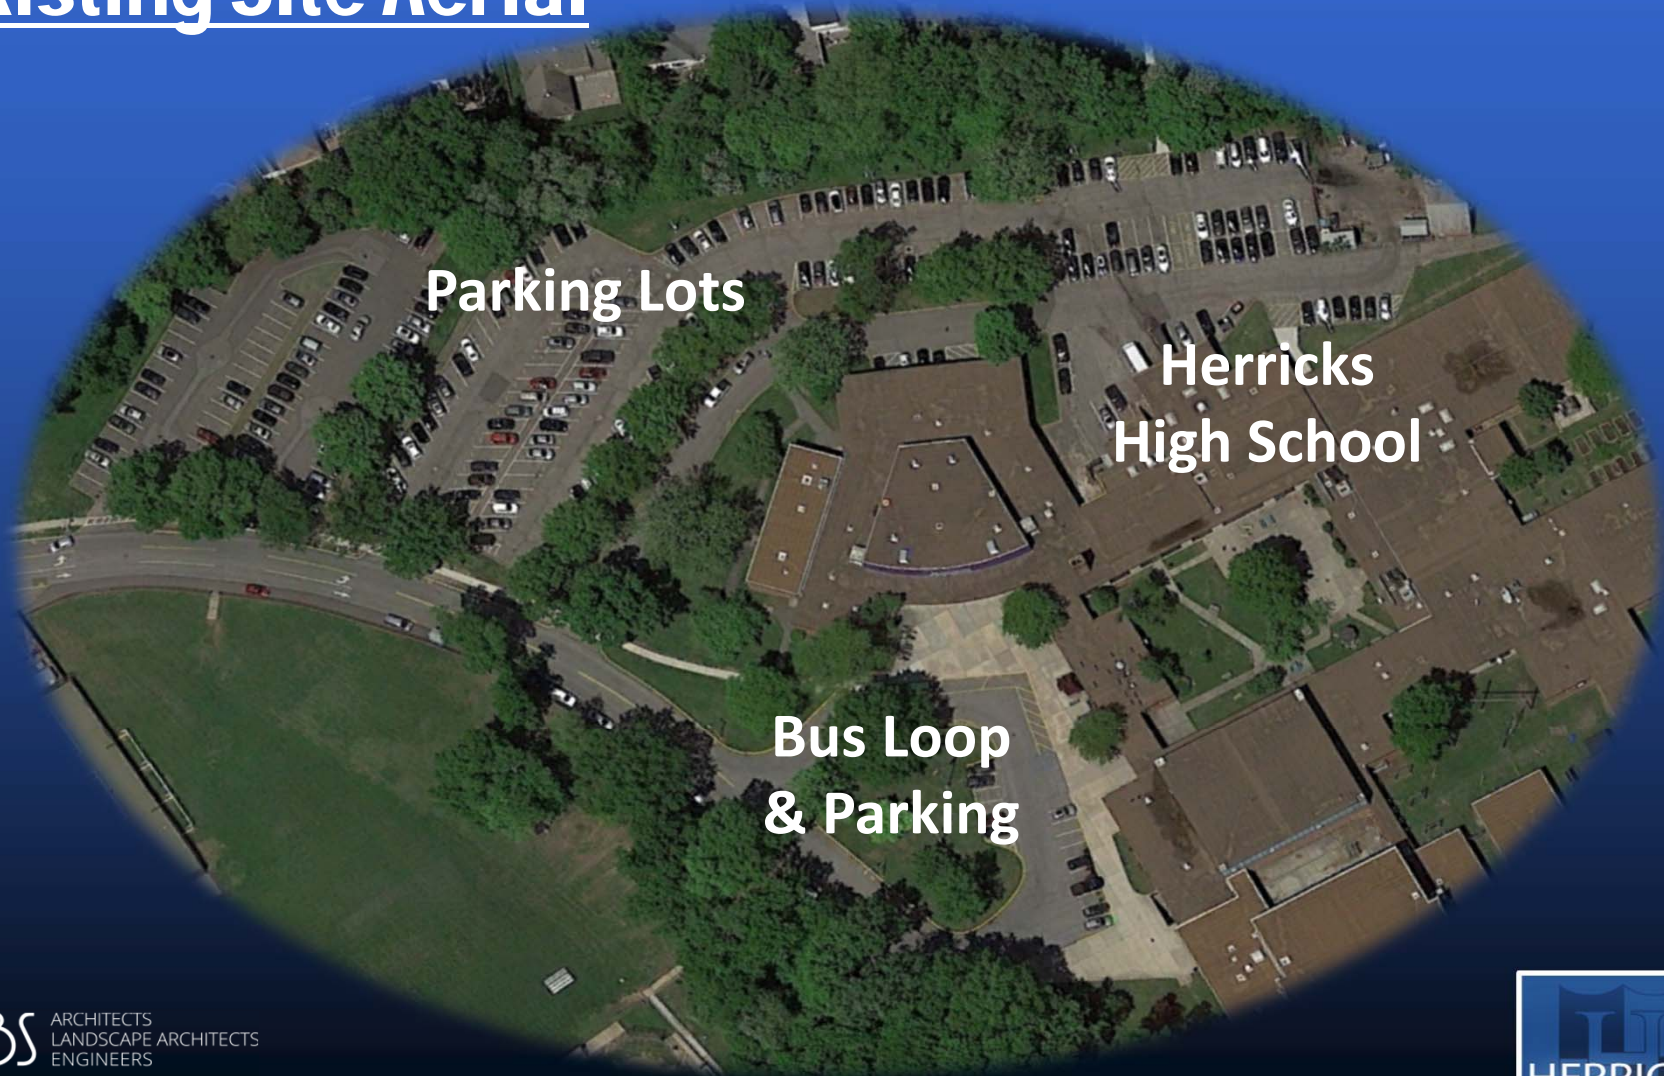

Phase IV Projects – to be re-bid

Parking Lot Improvements

Herricks High School

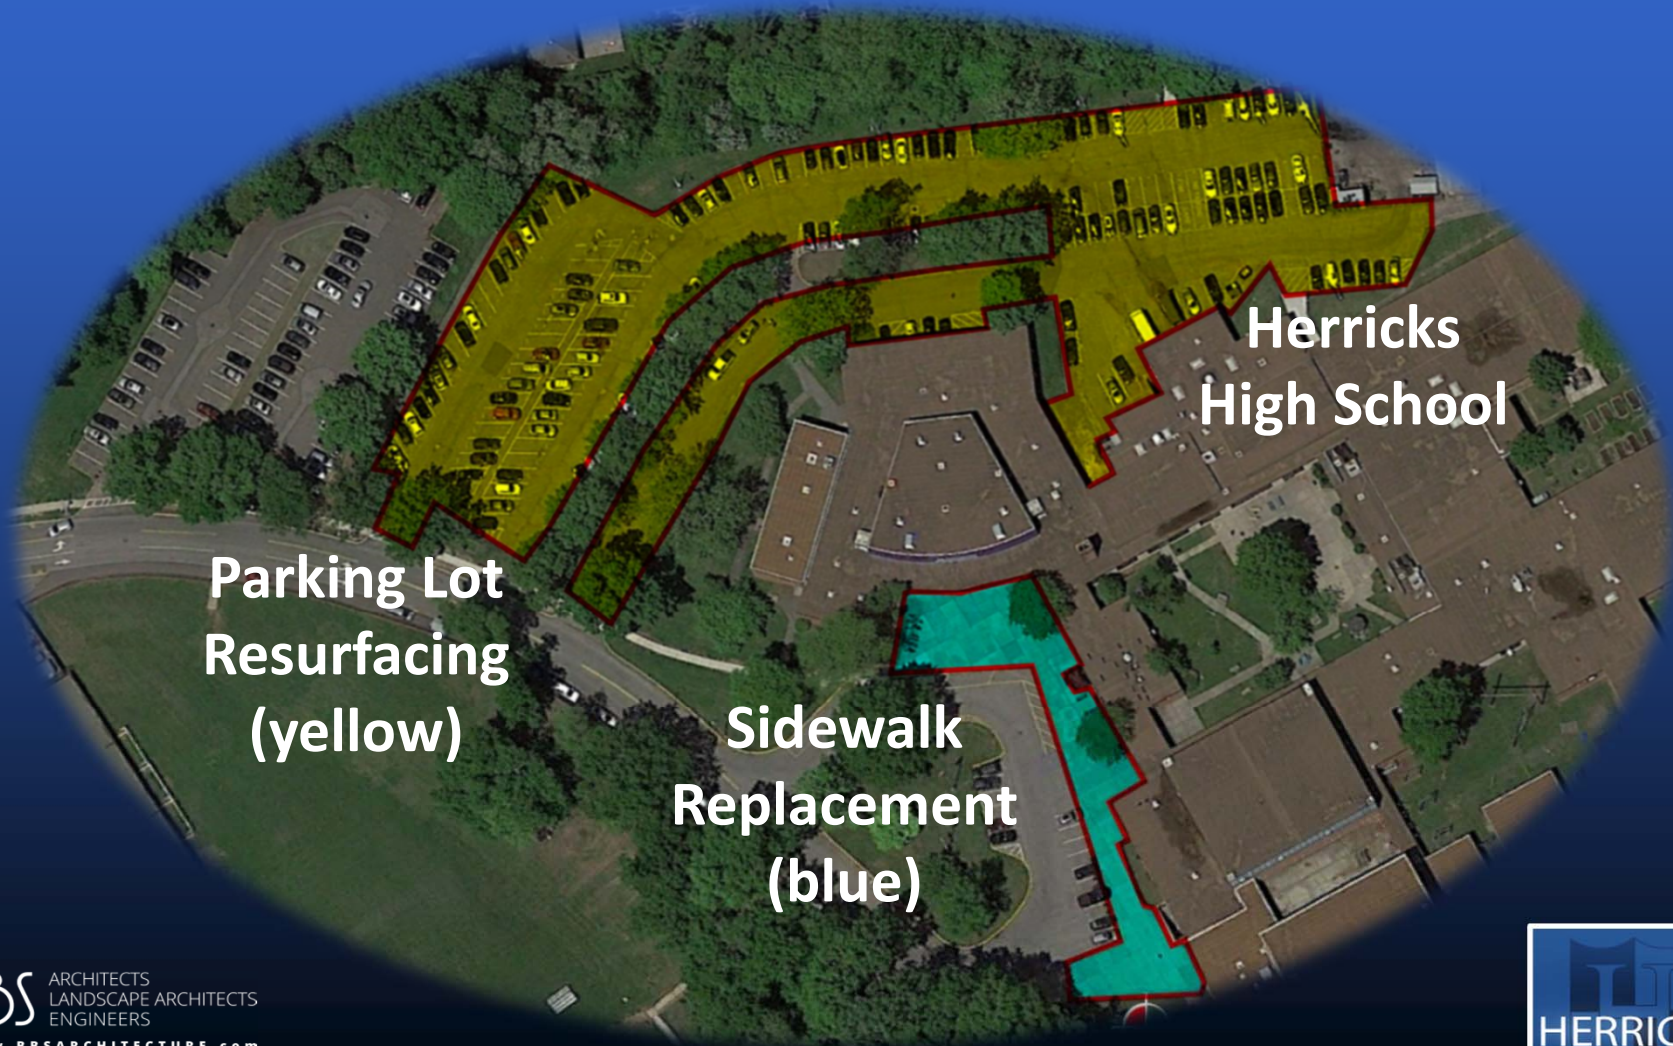


Parking Lot
Resurfacing
(yellow)

Sidewalk
Replacement
(blue)

Phase IV Projects – to be re-bid

Existing Bus Loop Aerial


Herricks High School

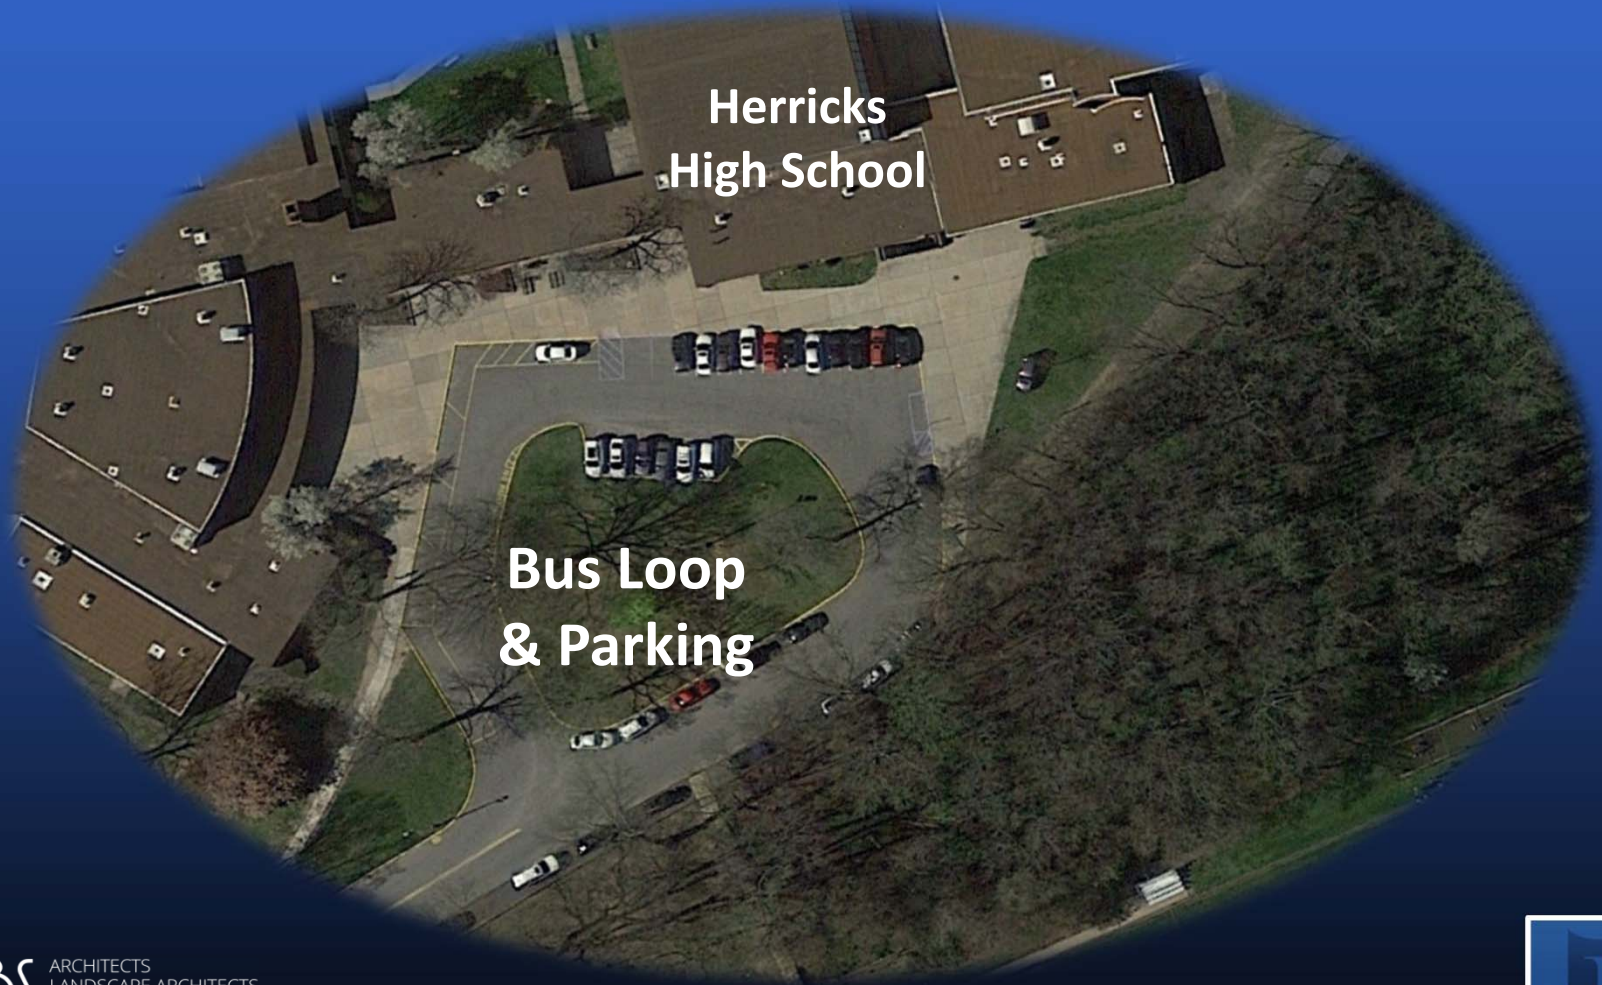

Phase IV Projects – to be re-bid

Herricks High School

Bus Loop Schematic Plans

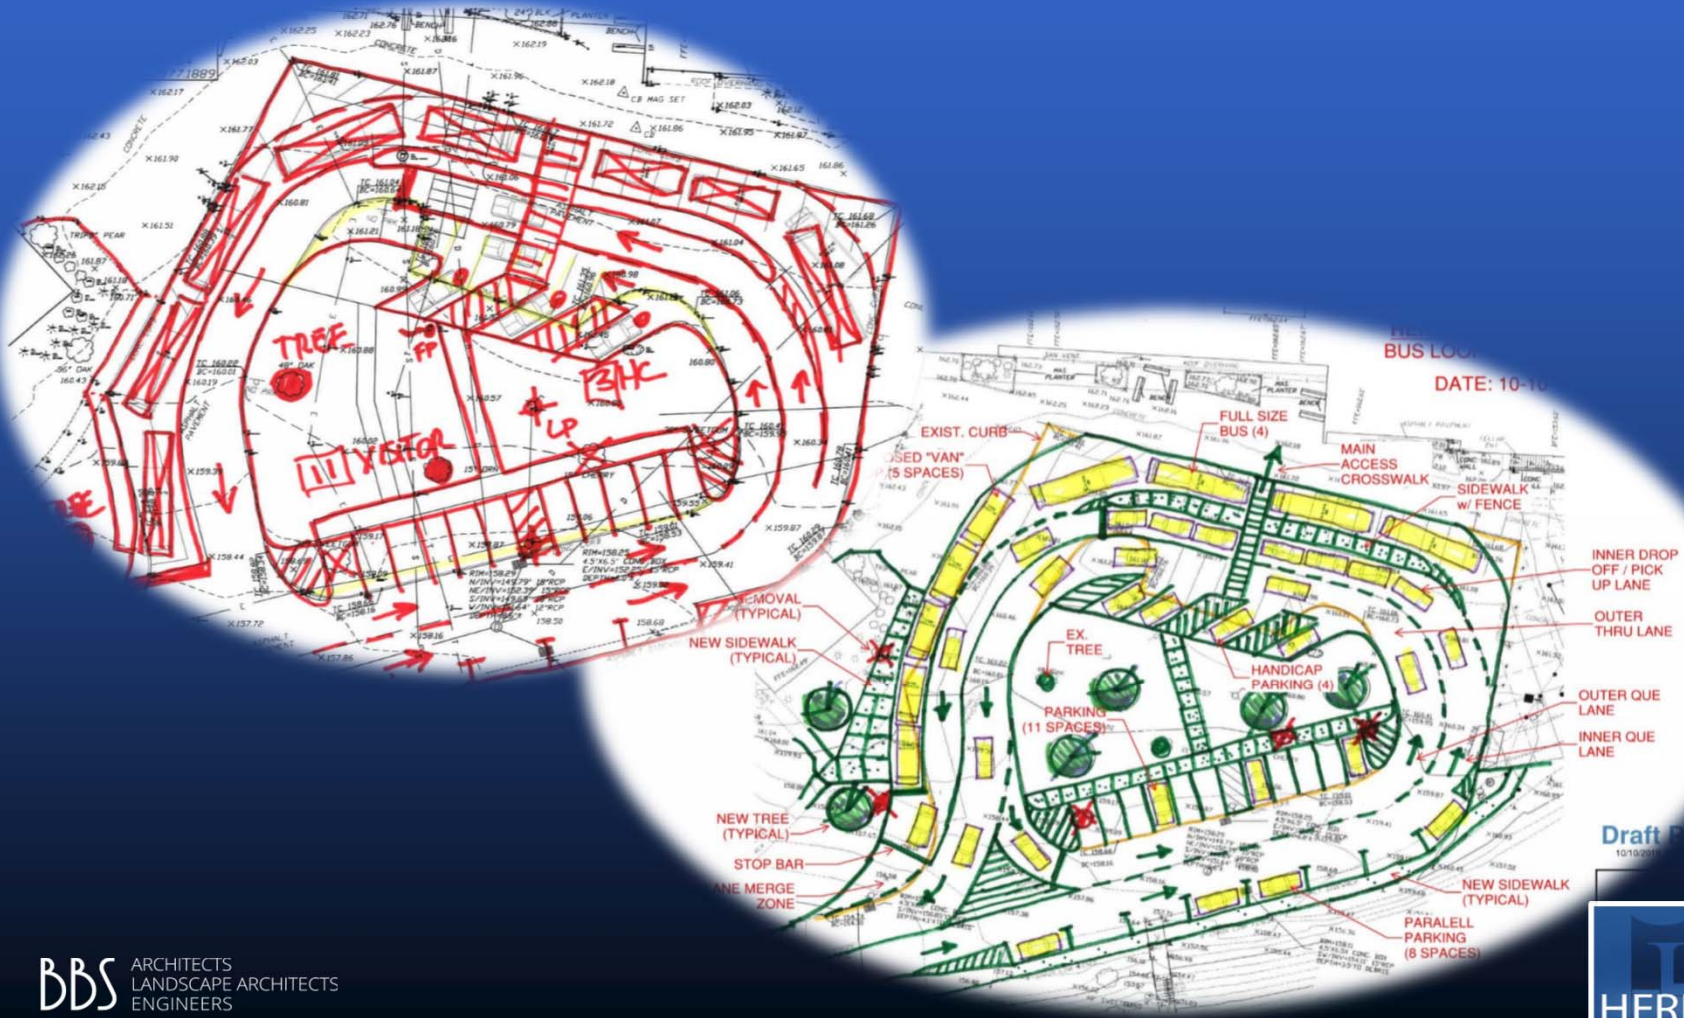

Phase IV Projects – to be re-bid

Herricks High School


Bus Loop Consensus Plan



Phase IV Projects – to be re-bid

Herricks Middle School

Existing Site Aerial

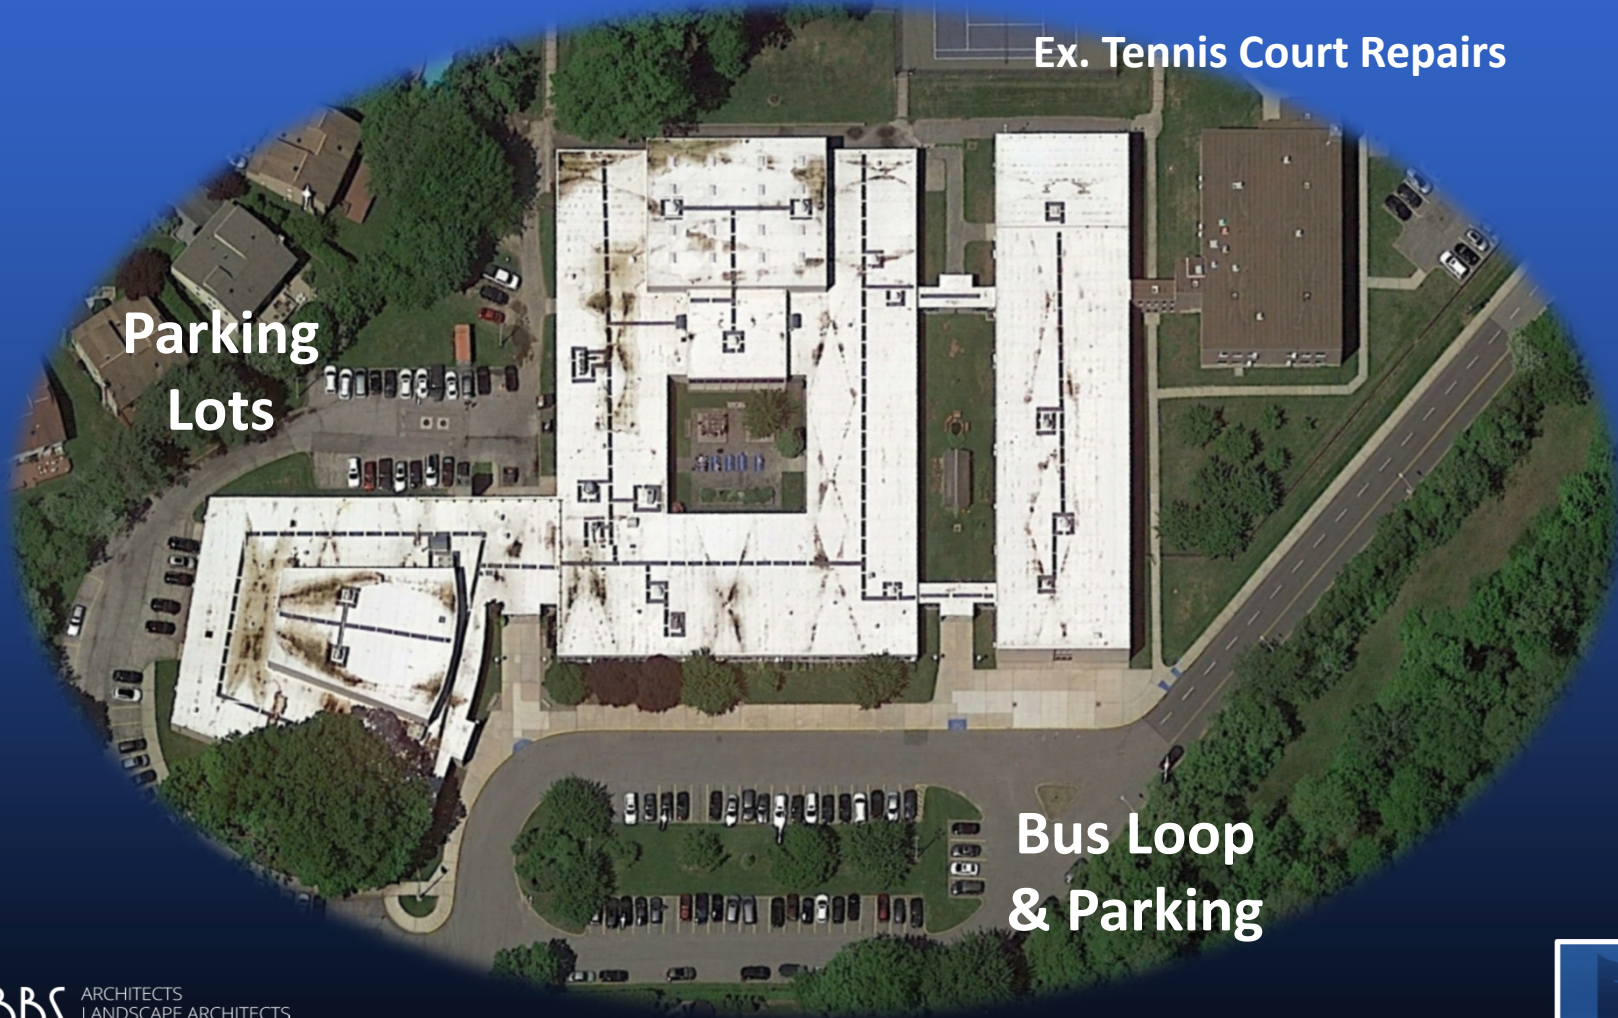

BBS ARCHITECTS
LANDSCAPE ARCHITECTS
ENGINEERS
www.BBSARCHITECTURE.com




Phase IV Projects – to be re-bid

Herricks Middle School

Parking Lot Improvements

Partial Parking Lot Resurfacing
(yellow) – done in Spring, 2019 via state
contract

Ex. Tennis Court
Repairs (blue)

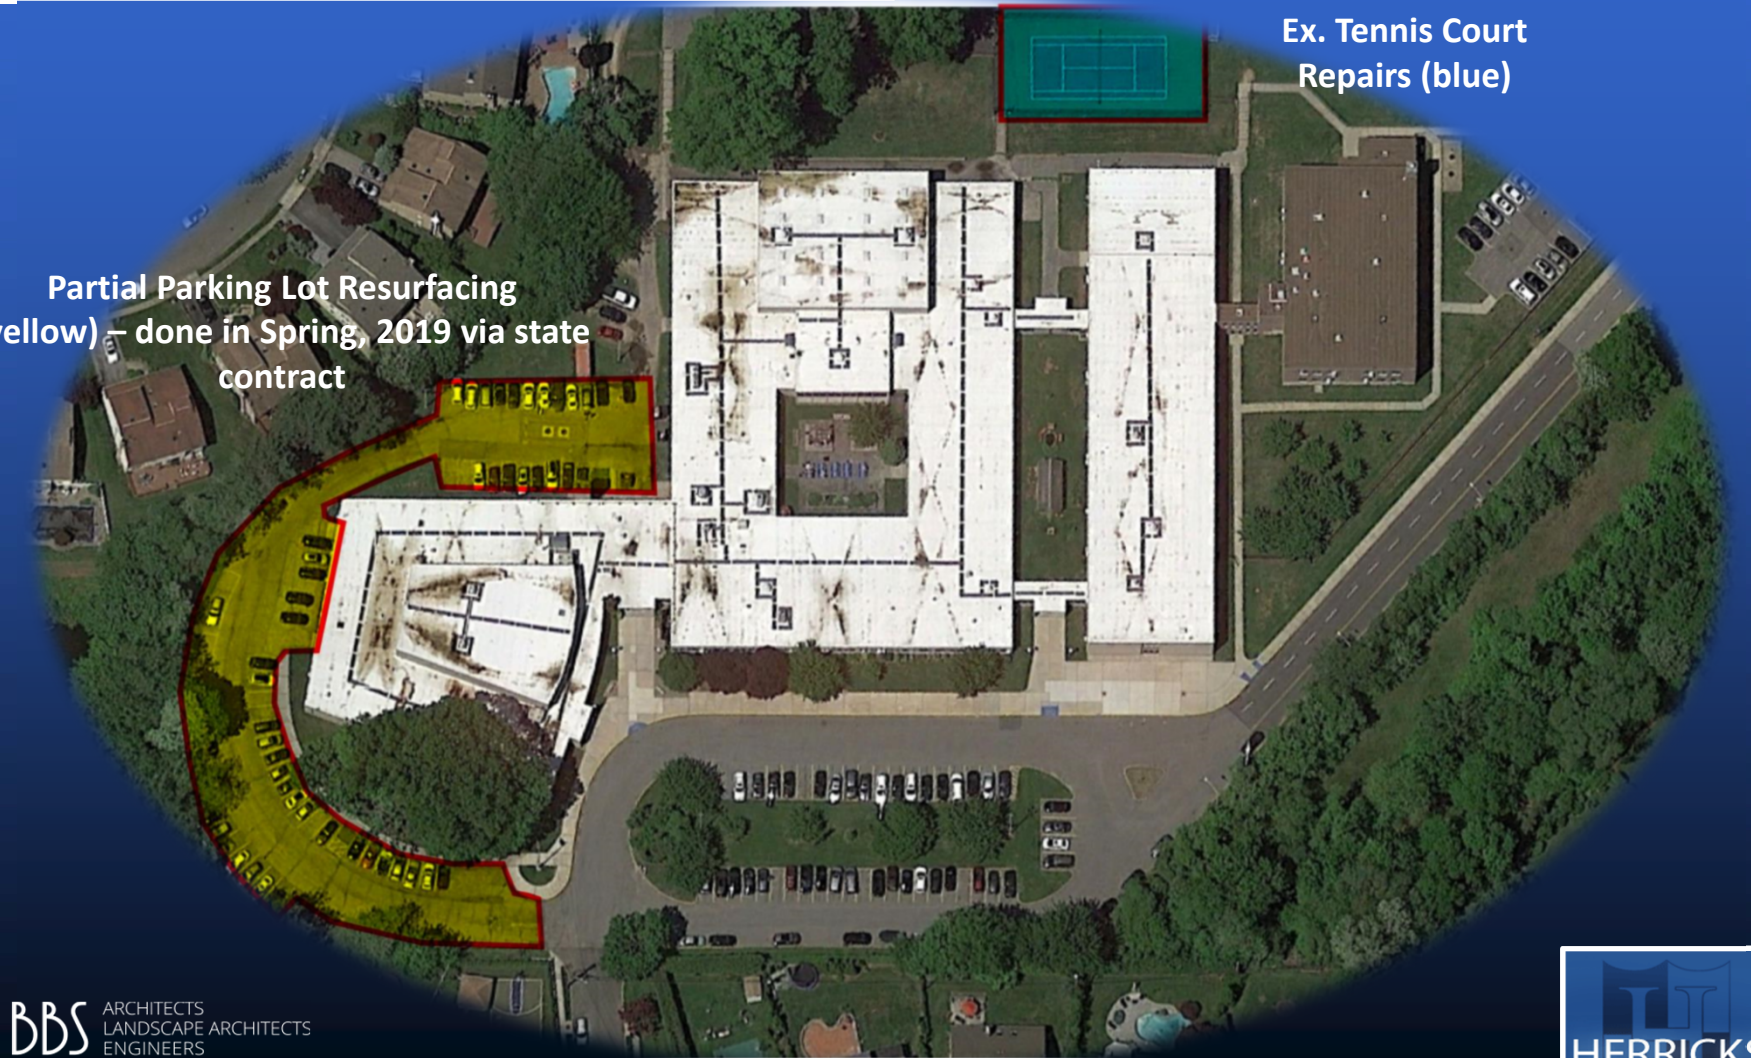

Phase IV Projects – to be re-bid

Herricks Middle School

Existing Bus Loop Aerial




Bus Loop & Parking

Phase IV Projects – to be re-bid

Herricks Middle School

Bus Loop Schematic Plans

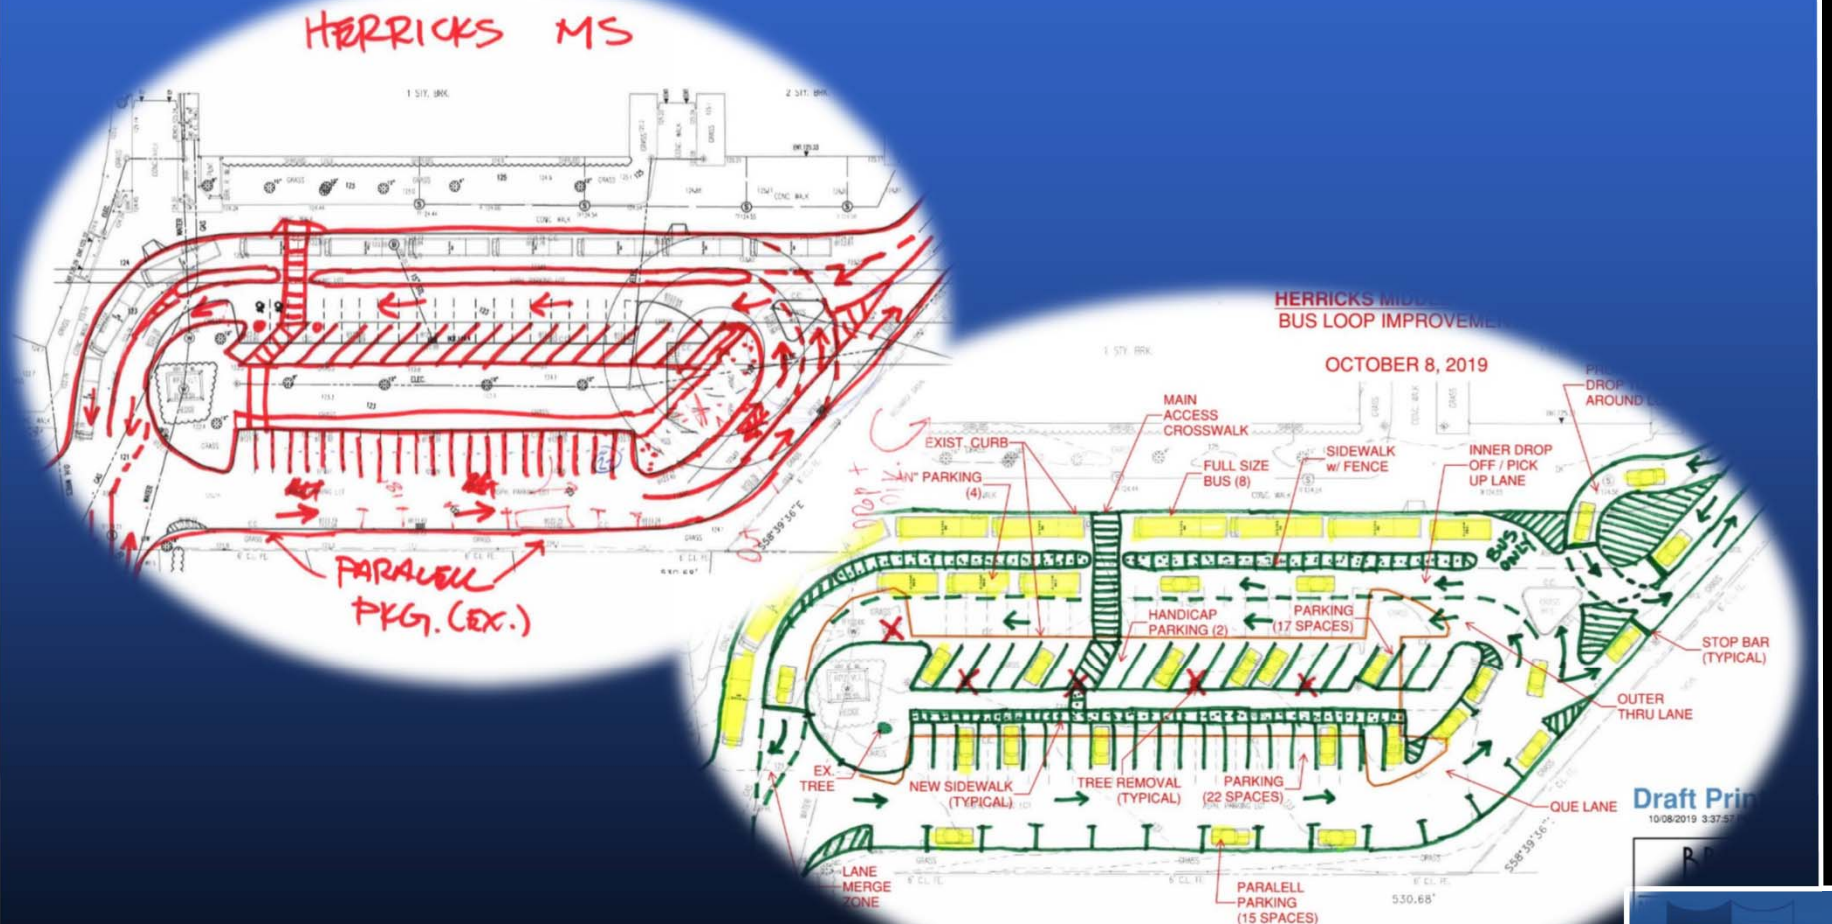

Phase IV Projects – to be re-bid

Herricks Middle School

Bus Loop Consensus Plan



Phase IV Projects – to be re-bid

Timeline for these sitework projects was originally proposed as:

Bidding / Contracts

May/June 2020

Construction

High School Parking

Summer 2020

Middle School Bus Loop & Tennis Courts

~~Summer 2020~~

High School Bus Loop

Summer 2021

To be re-bid and re-scheduled

Phase IV Project – New High School Fitness Center


The new Fitness Center was initially set to public bid on February 6, 2020, with the bids due on March 5, 2020.

Due to the onset of COVID-19 conditions, the BOE deemed the project as “non-essential” in conformance with the pandemic guidelines that were set in place by the state. All bids were formally rejected by the BOE, and project was put on hold for a re-bid which took place on July 16, 2020.

On October 8, 2020, the District awarded (4) prime contracts for General Construction & Sitework, Mechanical Construction, Plumbing Construction and Electrical Construction. Contracts recently executed and project kick-off meeting took place in late October. Substantial Completion date is scheduled for October, 2021.

District Construction Manager Park East Construction will elaborate further on the proposed construction schedule.

Phase IV Project – New High School Fitness Center

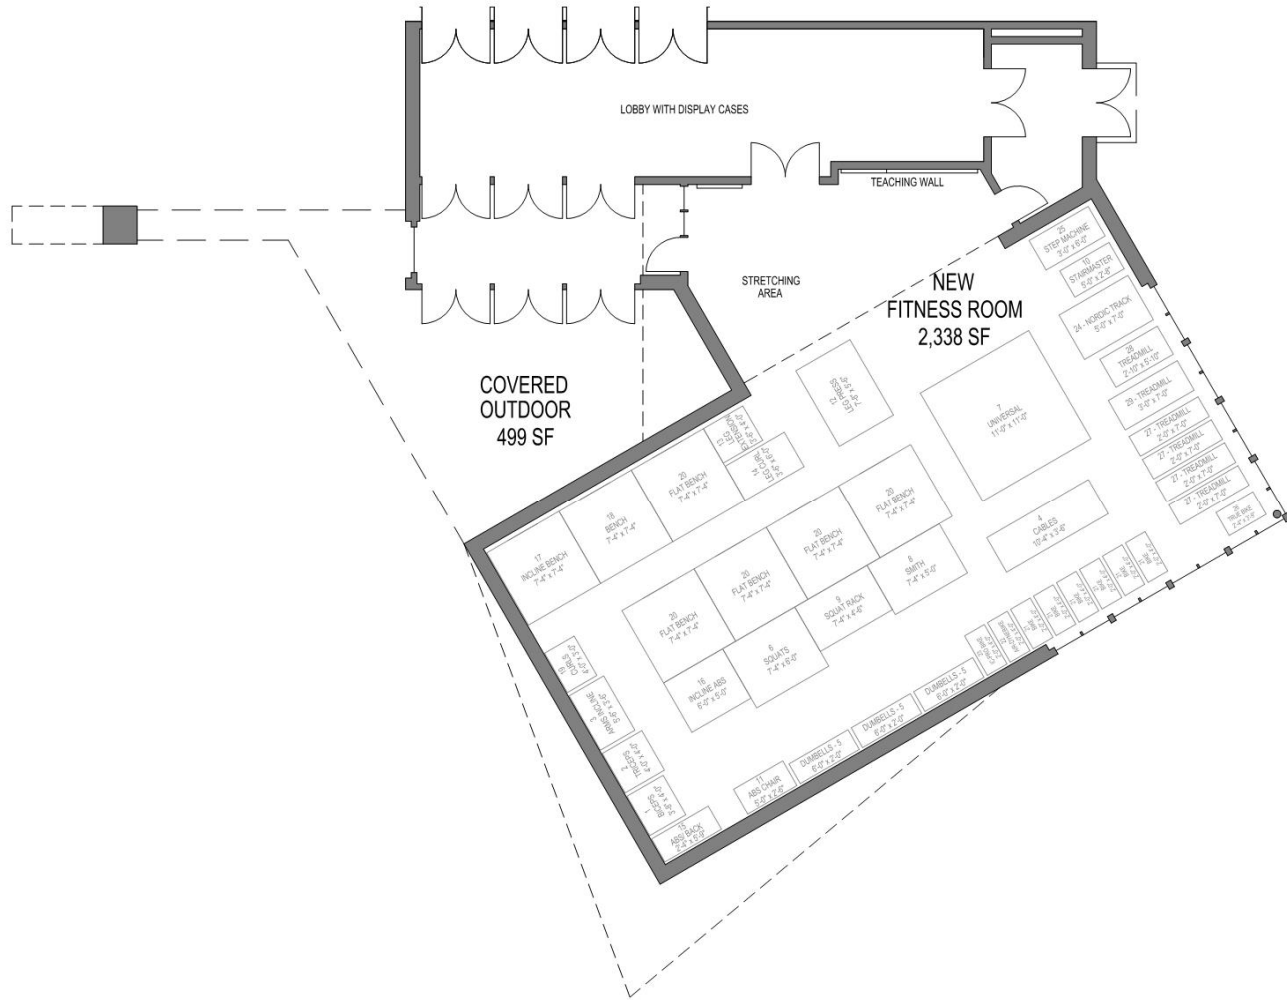

Phase IV Project – New High School Fitness Center



New High School Fitness Center – Exterior Elevation

Phase IV Project – New High School Fitness Center



BBS ARCHITECTS
LANDSCAPE ARCHITECTS
ENGINEERS
www.BBSARCHITECTURE.com

New High School Fitness Center – Interior Elevation



Phase IV Project – New High School Fitness Center



BBS ARCHITECTS
LANDSCAPE ARCHITECTS
ENGINEERS
www.BBSARCHITECTURE.com

New High School Fitness Center – Interior Elevation



Herricks Union Free School District

Thank You
