Herricks Union Free School District

2016 Capital Improvements Bond Update

August 31, 2017



Timeline to Date

December 6, 2016 Successful Bond Referendum Vote

December, 2016 BBS conducts field survey of existing interior doors and hardware with District Facilities

January, 2017 Director, and prepares construction documents for Phase I Capital Improvements.

Synthetic turf field drawings are prepared and added to Phase I Capital Improvements package

February 21, 2017 Executed paperwork mailed to SED; Phase I logged in February 23, 2017

March 23, 2017 BBS Update to Board of Education

May 25, 2017 BBS Update to Board of Education

BBS received a "Level 1" review for Phase I on April 4, 2017. Reviewed on May 8, 2017

Pre-Bid Addendum to SED sent; SED requires update on NYSOPHP for Shelter

Rock Academy, which is on Historic Register. SHPO approval obtained on July 18, 2017;

information forwarded to SED on July 18, 2017; currently awaiting final SED approval

for late Summer, 2017 bidding as planned. SED Approval obtained; projects went to bid

June 9, 2017 Phase II SED project submission made June 12. "In the queue" for review.

July 20, 2017 BBS Update to Board of Education – Cafeteria Interiors

August 4, 2017 Phase I Capital Improvements released to bid; Bids taken on 8/23/17.



Phase II projects included in June, 2017 submission

- High School Cafeteria & Kitchen Renovations
- New 1,600-seat Bleachers and New Press Box at High School
- New Comfort Station Building at High School
- New Sports Storage Building at High School
- New Running Track Lighting at High School

Phase II projects included in Fall, 2017 submission

- Existing Concession Stand Rehabilitation at High School
- Selective Electrical Upgrades (service replacement) at High School
- Localized Ventilation Improvements all schools
- Localized site drainage, asphalt & sidewalk improvements all schools



Bleacher Fit-Out Options

8/23/17 - A meeting was held at District to discuss the different fit-out options available for the new 1,600-seat bleachers/grandstand scheduled for Phase II construction, Summer 2018. Attendees included District representatives (High School Principal and Vice Principal, Athletic Director, Facilities Director & staff, Assistant Superintendent for Business, District Superintendent & Board President, as well as BBS Architects, Landscape Architects & Engineers, PC, and Park East Construction.)

Discussion centered around possible 'fit-out' options for the proposed bleachers, and some initial discussion revolving around the proposed grandstand drop-off area, which will be located off the main entry/exit drive leading up to the High School building. These items will undergo continued review and final selections from District representative, including the Board members.

Any selected 'fit-out' options will be included into the final bid set of Phase II documents as Add Alternates to contract, so that if the base bid for the bleachers comes in less than budgeted, the additional items can be considered and awarded.



Bleachers - Standard Fit-Out



The bond budget for the 1,600-seat aluminum bleacher assembly includes base/standard fit outs similar to that shown below; standard aluminum bench seating with colored front skirt.




Bleachers - Standard Fit-Out



Another example of standard aluminum bench seating with colored front skirt.



Grandstand – Seat Riser / Seat Back Options

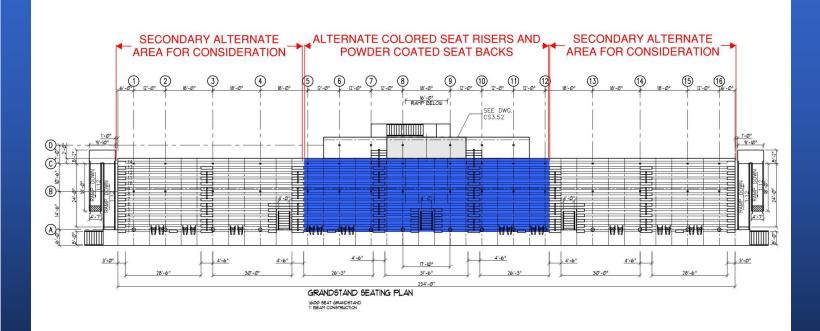

A common Add Alternate to Base Bid could be adding colored seat risers and powder-coated seat backs, routinely set at the center section. Additional Add Alternates can also be taken for the seat backs at the remaining sections.




Grandstand – Seat Riser / Seat Back Options





Grandstand – Seat Riser / Seat Back Options

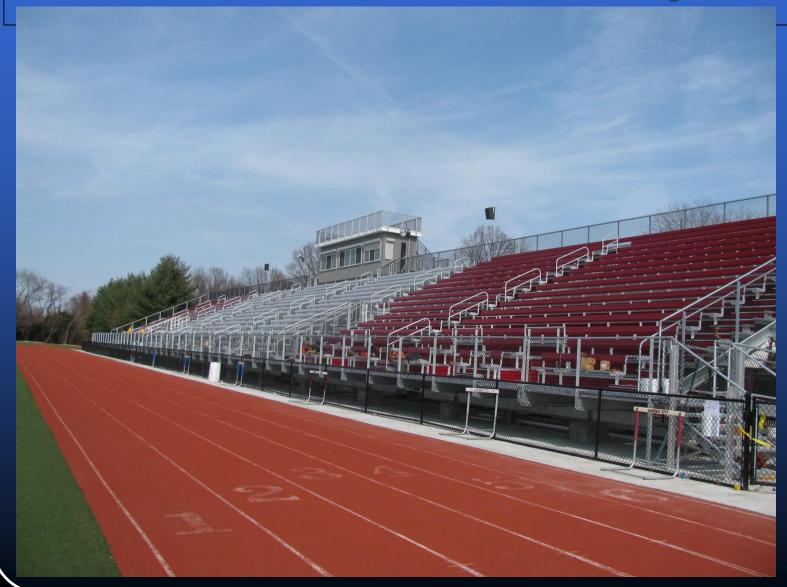



Grandstand – Standard Rear View



The standard rear view of Grandstand bleachers assembly. Exposed structure with chain link fence surrounds with privacy slats, flanking the vomitory entrances up into the stadium area. This is provided within the current bond




Grandstand – Upgraded Rear View



An upgrading of the standard exposed column treatment, rear view of Grandstand bleachers assembly. While an additional cost, the inclusion of brick pier surrounds and precast stone caps provide an upgraded style to the columns. Additional treatment can also include wrought iron fencing in lieu of black vinyl chain link fencing.



Grandstand – Drop-Off Plaza

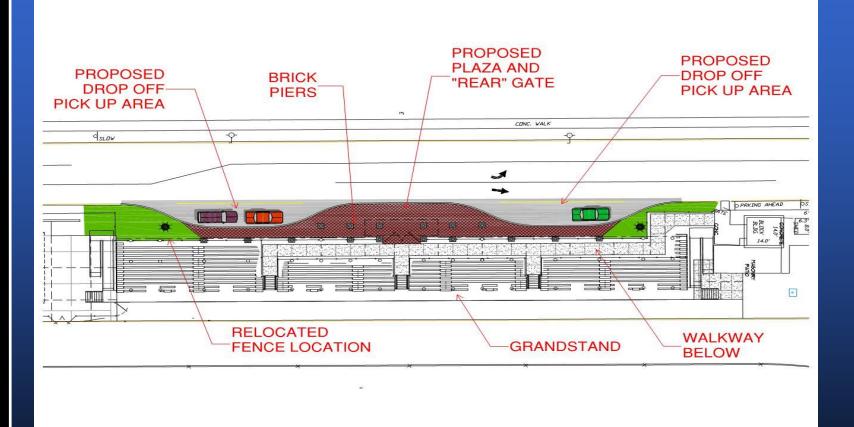

At 8/23/17 Owner's Meeting, discussion began on potential Grandstand drop-off plaza improvements – these site improvements would retain traffic flow on the existing entry drives to the High School entrance.



Bleacher Fit-Out Options – Proposed Costs

<u>ltem</u>	Estimated Add Alternate Cost
Bleacher Seat Backs (center 3 sections)	\$ 18,000
Bleacher Seat Backs (L & R 4 sections)	\$ 25,000
Bleacher Colored Risers (center 3 sections)	\$ 10,000
Bleacher Colored Risers (L & R 4 sections)	\$ 15,000
Brick Pier Surrounds & Stone Caps – 8' height	\$ 64,000
Ornamental Wrought Iron Fencing	\$ 30,000
Drop-Off Plaza Development	\$ 150,000



Herricks Union Free School District

Thank you

